

Project Status Report.

Project Summary:

Milestones: Forecast Date (Baseline Date)

Mobilize: June 3, 2024 (Actual May 29, 2024)

Foundation Complete: July 29, 2024 (Actual June 20, 2024)

Structure Complete: August 27, 2024 (Actual Aug 23, 2024)

Drywall Complete: December 19, 2024

Testing & Commissioning: April 11, 2025

Substantial Performance: April 25, 2025

Schedule Notes:

- **Concrete Testing – Cylinders Cast, testing ongoing**
- **Structure Inspection – Tentative Thursday Aug 29th**
- **M&E Rough In Inspection – Tentative Thursday Aug 29th**

Risk Registry:

- **Nothing to report at this time.**

Project Update:

August 12, 2024 - August 23, 2024

- Shop Drawing submissions / reviews ongoing
- Truss and roof sheathing completed
- Interior partitions and wood strapping completed
- Roof membrane completed
- Mechanical & Electrical Rough-ins started and ongoing
- Tyvek installation completed
- Hydro trench from building to pole completed

Aug 26 to Sept 6, 2024

- Shop Drawing submissions / Reviews.
- Window and door blueskin
- Window and door installation
- Complete Mechanical & Electrical rough-ins
- Civil site services
- Septic system start

**2 week
look ahead**



Progress – Structure & Roof Membrane



Progress – Structure & Roof Membrane



Progress – M&E Rough-in




Progress – M&E Rough-in

Progress Photos.





Progress – Exterior weather barriers

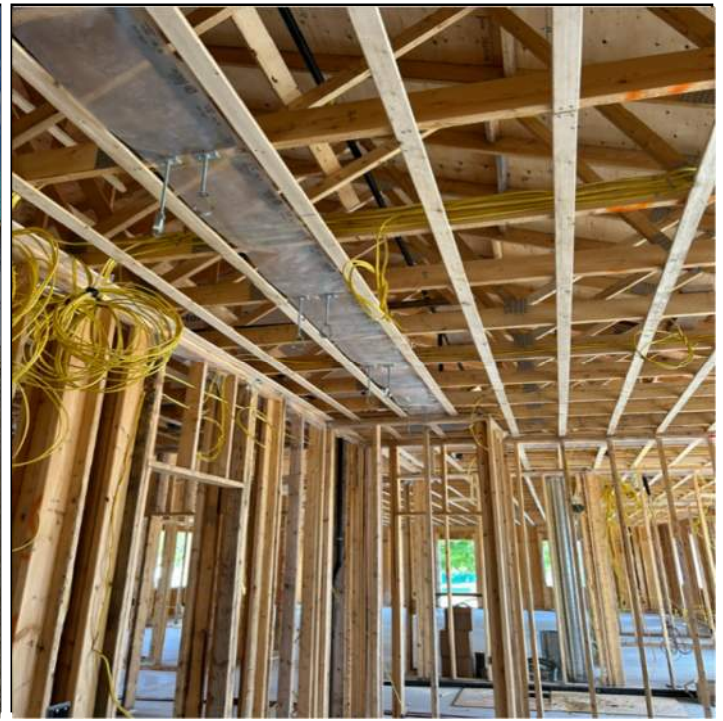

Progress – Interior framing / rough-ins



Progress – Wood strapping / rough-ins in Library



Progress – Wood strapping / rough-ins in Hall

Progress Photos.

CAVANAGH
GENERAL CONTRACTING
